


REVO

KELOWNA

Construction Update March, 2025

Building Type **Condo** # of floors **6** # of units **240** Location **Kelowna, B.C.**

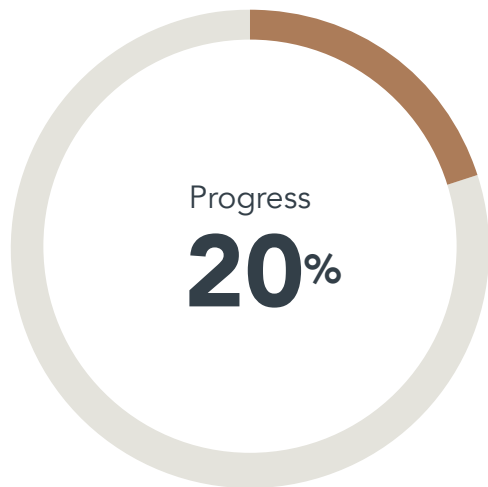

REVO Kelowna is progressing on schedule, with the parkade forming and pouring well underway and all civil utility work completed, both on and offsite. The majority of the slab on grade concrete has been completed and the suspended slab for the first level of parkade is now 60% complete, including the internal ramp connecting the two parkade levels. Rough-ins continue on the northern portion of the suspended slab, while several columns on the southern suspended slab, which connects the second level parkade, have already been completed. The site transformer has been installed, with permanent power scheduled to be connected before the end of February. Prefabrication of wall panels has begun offsite with the first floor set for delivery in April.

